

SE Lab 2 - Agile Project Management with Jira

Project: Automated Rubric Assignment Evaluator (Problem Statement 02, from Lab 1)

Name: Ojas Binjola

SRN:PES1UG24CS307

What I built

I made a company-managed Scrum project in Jira with the key ARAE. It has 5 epics and 14 user stories, 68 story points in total. The epics follow the same five requirement areas I wrote in Lab 1.

- EPIC-1 Submission Intake and Validation (FR-003)
- EPIC-2 Automated Evaluation and Rubric Scoring (FR-001, NFR-001, NFR-002)
- EPIC-3 Rubric Configuration and Versioning (FR-002)
- EPIC-4 Automated Peer Review Distribution (FR-004)
- EPIC-5 Score Override and Audit Trail (FR-005)

I then ran two one-week sprints on the board.

Sprint 1: 31 points planned, 31 done

Goal: a student can submit a valid archive and get an itemised rubric score automatically.

Key	Story	Priority	Points	Status
ARAE-6	1.1 Upload project archive	High	3	Done
ARAE-7	1.2 Format and size validation	High	5	Done
ARAE-8	1.3 Rule-specific rejection message	Medium	2	Done
ARAE-9	2.1 Auto-queue and run test suite	High	8	Done
ARAE-10	2.2 Itemised rubric breakdown	High	5	Done
ARAE-13	3.1 Author a rubric	High	5	Done
ARAE-14	3.2 Rubric weight validation	High	3	Done

Sprint 2: 37 points planned, 31 done

Goal: safe execution at scale, plus peer review and overrides.

Key	Story	Priority	Points	Status
ARAE-11	2.3 Sandboxed execution	High	8	Done
ARAE-12	2.4 Handle 100 concurrent submissions	Medium	5	Done
ARAE-15	3.3 Rubric versioning	Medium	5	Done
ARAE-16	4.1 Auto-assign peer reviewers	Medium	8	Done
ARAE-18	5.1 Override with justification	Medium	5	Done
ARAE-17	4.2 No self-assignment rule	Medium	3	Not done
ARAE-19	5.2 Immutable audit log	Low	3	Not done

1. Did the estimations match the actual effort?

Mostly yes. The three 8-point stories (2.1, 2.3 and 4.1) were the hard ones, and I was right to mark them as big. Each of them needs a design decision, not just code.

Two estimates were off:

- 1.3 was too high at 2 points. Once 1.2 had already checked the file and knew why it failed, printing the exact rule was a small change.
- 4.2 was too low at 3 points. It looks like a one-line filter, but it is really a rule inside the allocation logic of 4.1, so it could not be finished on its own.

So the lesson is that a story which only exists as a constraint on another story is not independent, and sizing it separately gives a number you cannot hit.

2. Was the backlog well prioritised?

Mostly. All the High items (upload, validation, auto evaluation, breakdown, rubric authoring and weight check) are the minimum needed for the system to produce a mark, and they all went into Sprint 1. Override and audit log were kept low, which is fine, because there is nothing to override until scores exist.

One thing I would change: 3.2 (weight validation) should have come before 2.2 (rubric breakdown). If the weights do not add to 100 percent, the breakdown is wrong and it is hard to notice.

3. How did the sprint execution match the plan?

Sprint 1 went as planned. Everything I committed got done, so my measured velocity was 31 points.

For Sprint 2 I planned 37 points anyway, which was about 19 percent more than the only velocity number I had. It finished at 31 points again, and two stories carried over: 4.2 (3 points, still To Do) and 5.2 (3 points, In Progress).

The carry-over was not random. 4.2 depends on 4.1, and 5.2 depends on 5.1. When a sprint is over-committed, the work at the end of a chain is what gets left.

4. What did the burndown show about capacity?

Sprint 1 burns down to zero. Sprint 2 drops to 6 points and then stays flat, because the last two stories never closed. That flat tail at the end is the 6 points I over-committed by.

One honest note: I ran both sprints in one sitting as a simulation, so the day-by-day slope of the line does not mean much. The useful part is where each line ends and how far it stays from the guideline.


Two things I would do next:

- Plan Sprint 3 at around 31 points, not 37, and pull in ARAE-17 and ARAE-19 first.
- Split the 8-point stories into 3 and 5 point pieces. An 8-point story shows no progress on the chart until it closes, so almost half of Sprint 2 was invisible until the end.

Links and screenshots

Jira site: <https://ojasbinjola.atlassian.net>, project ARAE, board "ARAE board".

✓ Jira work item



⚡ ARAE-3



> Development

> **More fields** Story Points, Original estimate, Time tracking, Components, Sprint, Team, Fix vers...

✓ Child work items



100% Done

Work	Pri...	Stor...	As...	Status
✓ ARAE-13 Story 3.1 Author a rubric	⬆ H.	5	👤 U	Done ▾
✓ ARAE-14 Story 3.2 Rubric weight validation	⬆ H.	3	👤 U	Done ▾
✓ ARAE-15 Story 3.3 Rubric versioning	⬆ M	5	👤 U	Done ▾

Linked work items

Add linked work item

Confluence content ⓘ



📄 Project plan

Try template

> **Automation** ⚡ Rule executions

Created 4 days ago

Updated 15 minutes ago

⚙ Configure

Activity

ARAE board

Summary Timeline Active sprints Backlog Calendar List Forms Development Docs

Take me to Reports Dismiss

OB Filter

16 completed in the last 7 days

21 updated in the last 7 days

21 created in the last 7 days

3 due soon in the next 7 days

Status overview
Get a snapshot of the status of your work items. View all work items

21
Total work item...

To Do: 5

Done: 16

Recent activity
Stay up to date with what's happening across the space.

OB Ojas Binjola(PES1UG24CS307) created 7 minutes ago

OB Ojas Binjola(PES1UG24CS307) created 8 minutes ago




OB Ojas Binjola(PES1UG24CS307) updated field "Start date" on 14 minutes ago

Priority breakdown
Get a holistic view of how work is being prioritized. How to manage priorities for spaces

Types of work
Get a breakdown of work items by their types. View all items

Type	Distribution
Epic	100%
Task	

Mon	Tue	Wed	Thu	Fri
31	Sept 1	2	3	4 ARAE Sprint 2 ARAE-3 EPIC-3 Rubric Configuration & Versioni... ARAE-4 EPIC-4 Aut...
7 ARAE Sprint 2 3 more	8 ARAE Sprint 3 3 more	9 3 more	10 3 more	11 3 more
14 ARAE-2 EPIC-2 Aut...	15	16	17	18
21	22	23	24	25
28	29	30	Oct 1	2

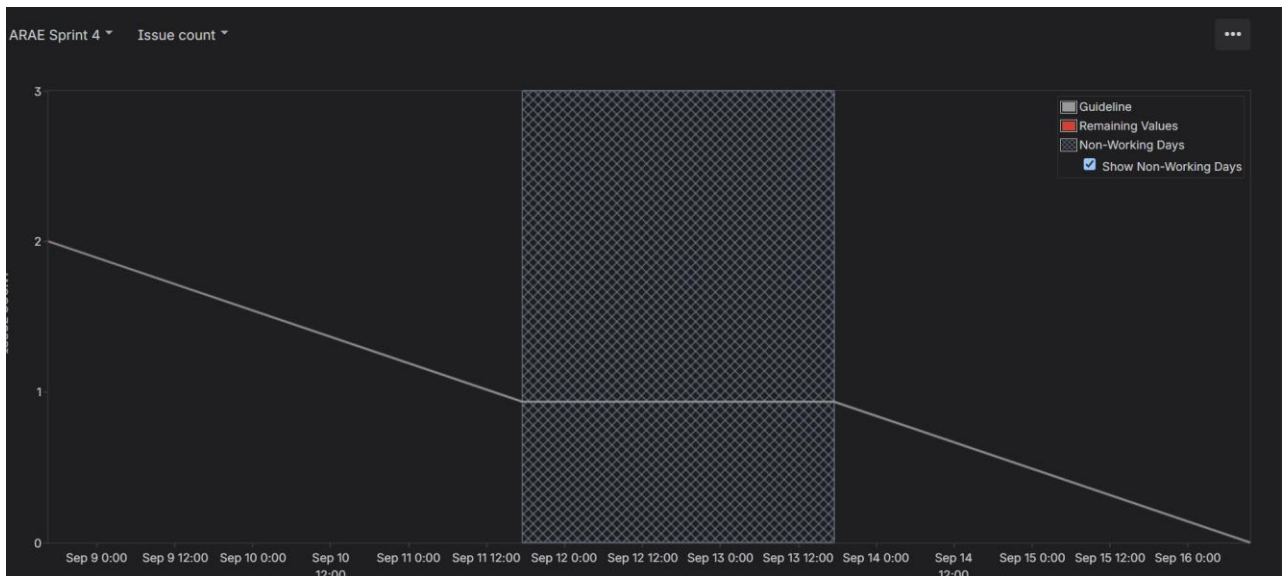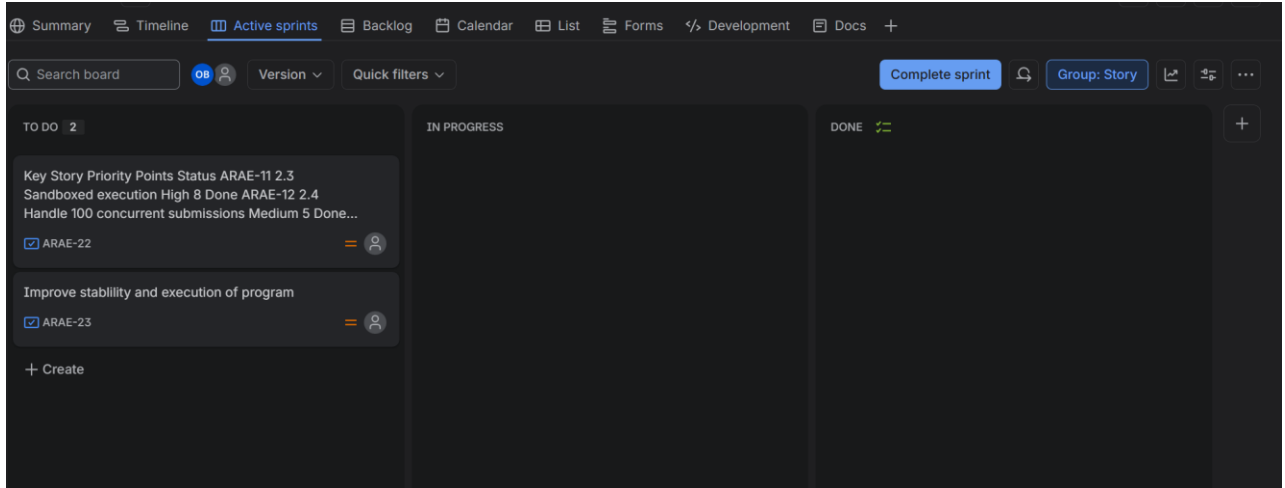

Screenshots attached: backlog with epics and stories, story points on the backlog, the active sprint board, and the burndown charts for both sprints.
